Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
February 2020 - January 2022

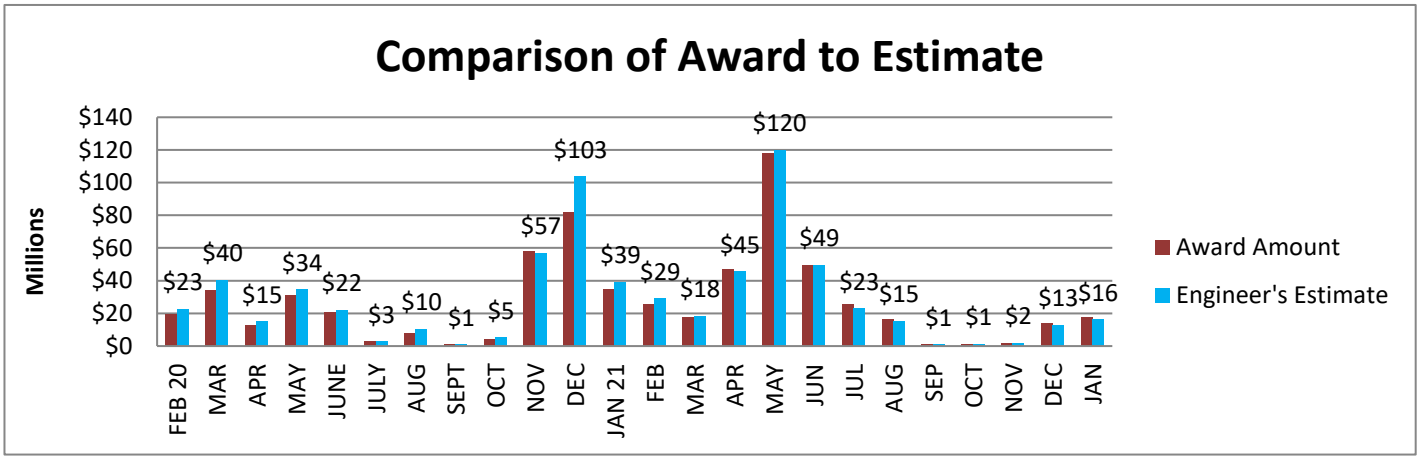

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
February 20	5	10	$22,617,249.00	$19,448,139.00	-14.0%
March	5	5	$40,184,808.00	$34,324,550.00	-14.6%
April	4	11	$14,815,642.00	$12,282,952.00	-17.1%
May	3	12	$34,337,191.00	$30,675,287.00	-10.7%
June	5	8	$21,904,179.00	$20,511,844.00	-6.4%
July	4	3	$2,502,440.00	$2,484,450.00	-0.7%
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
September	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
*January 22	4	4	$16,258,076.00	$17,566,886.00	8.1%

*Data not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison January 2022

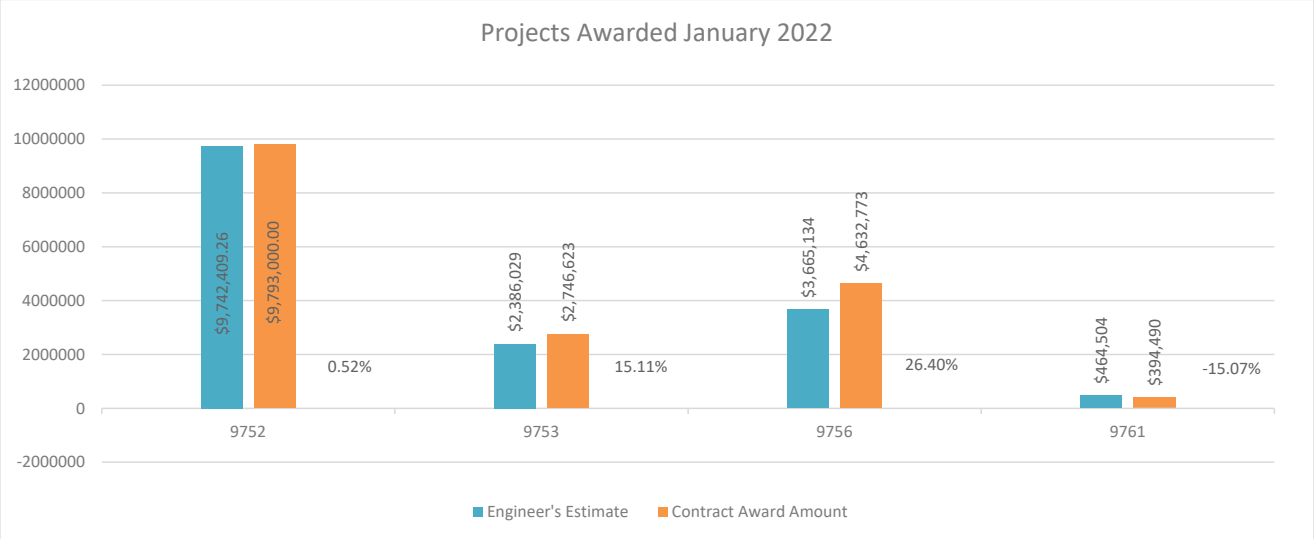

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9752	I-90, Dodson Rd To Adams County Line	1/20/2022	2	$9,742,409.26	$9,793,000.00	0.52%
9753	US 2 Et Al, NCR Bridge Patching 21-23	1/19/2022	4	$2,386,029	$2,746,623	15.11%
9756	SR 260 to Adams County Line - Paving	1/27/2022	3	$3,665,134	$4,632,773	26.40%
9761	Southworth Ferry Terminal Painting Pre	1/24/2022	5	$464,504	$394,490	-15.07%

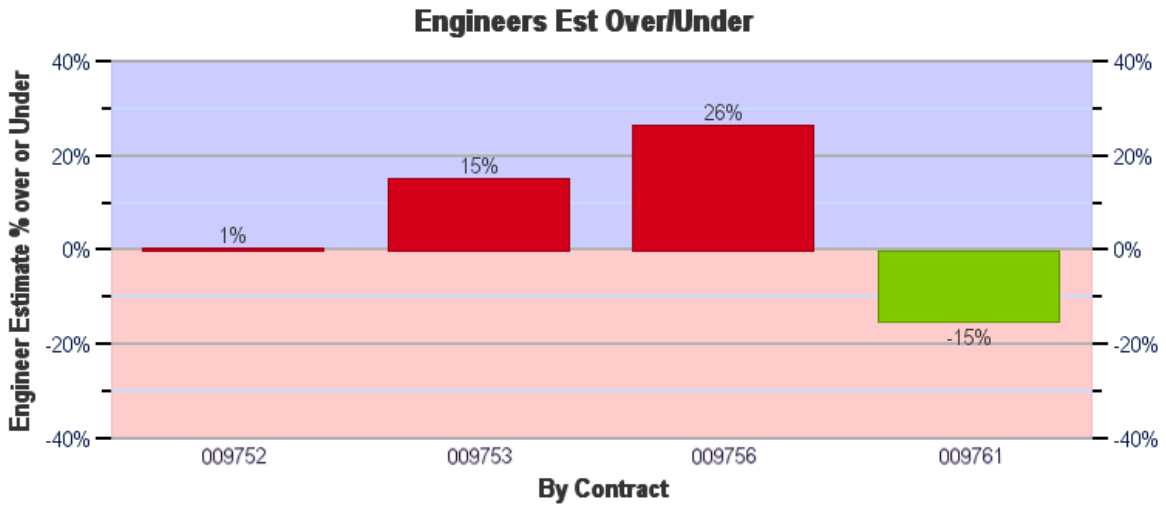

Data from January awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
March 2020 - February 2022

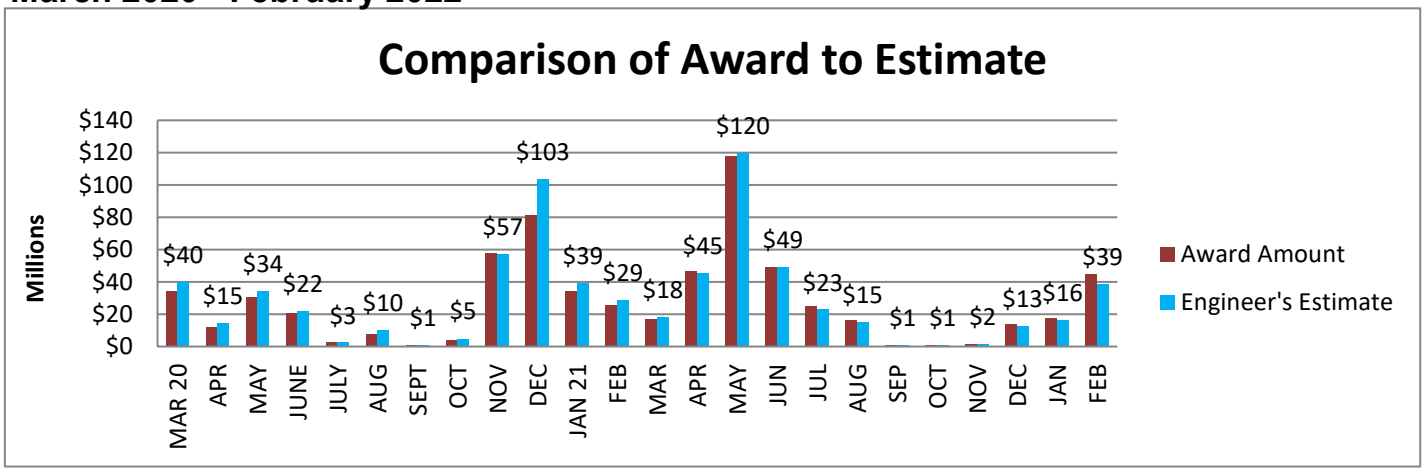

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
March 20	5	5	$40,184,808.00	$34,324,550.00	-14.6%
April	4	11	$14,815,642.00	$12,282,952.00	-17.1%
May	3	12	$34,337,191.00	$30,675,287.00	-10.7%
June	5	8	$21,904,179.00	$20,511,844.00	-6.4%
July	4	3	$2,502,440.00	$2,484,450.00	-0.7%
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
September	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
*January	4	4	$16,258,076.00	$17,566,886.00	8.1%
*February 22	4	6	$38,553,756.00	$45,096,911.00	17.0%

*Data not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison February 2022

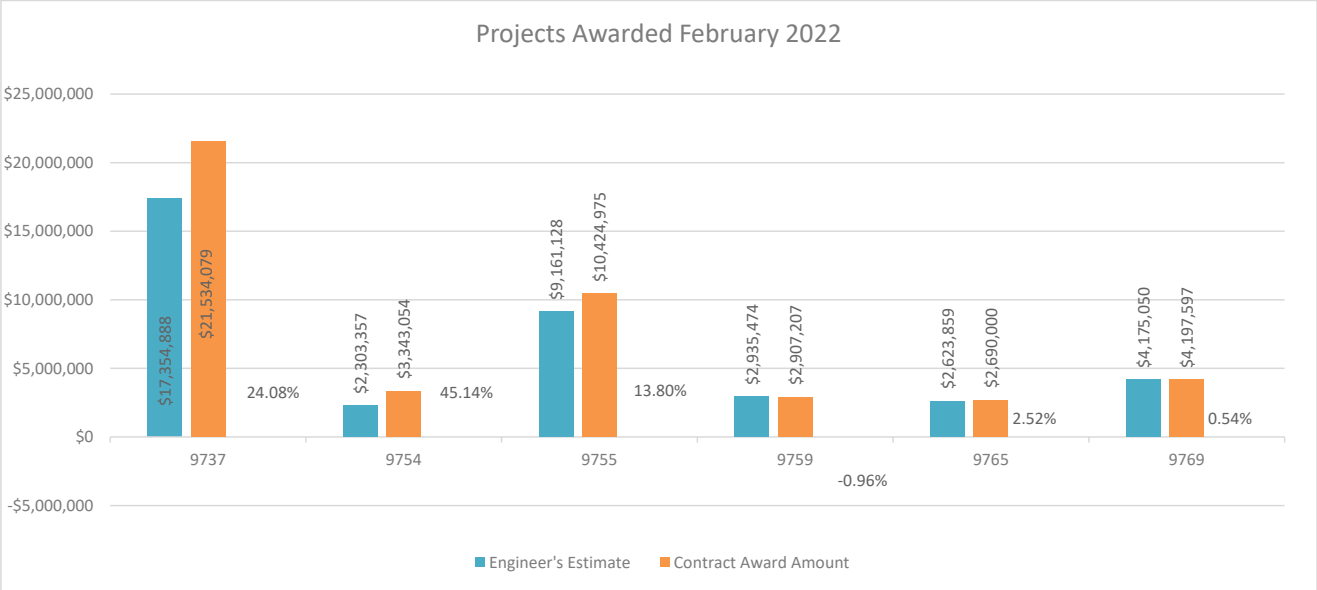

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9737	Bainbridge OHL Walkway Replacement & C	2/3/2022	9	$17,354,888	$21,534,079	24.08%
9754	Pepin Creek and Duffner Ditch Fish Passag	2/7/2022	3	$2,303,357	$3,343,054	45.14%
9755	SR 520 Vic I-5 Vic & SR 9 Vic Paving & ADA	2/1/2022	2	$9,161,128	$10,424,975	13.80%
9759	Davenport to Rearden Paving	2/1/2022	3	$2,935,474	$2,907,207	-0.96%
9765	Immel Rd to Arden Paving	2/17/2022	2	$2,623,859	$2,690,000	2.52%
9769	Skagit River Fish Passage	2/28/2022	4	$4,175,050	$4,197,597	0.54%

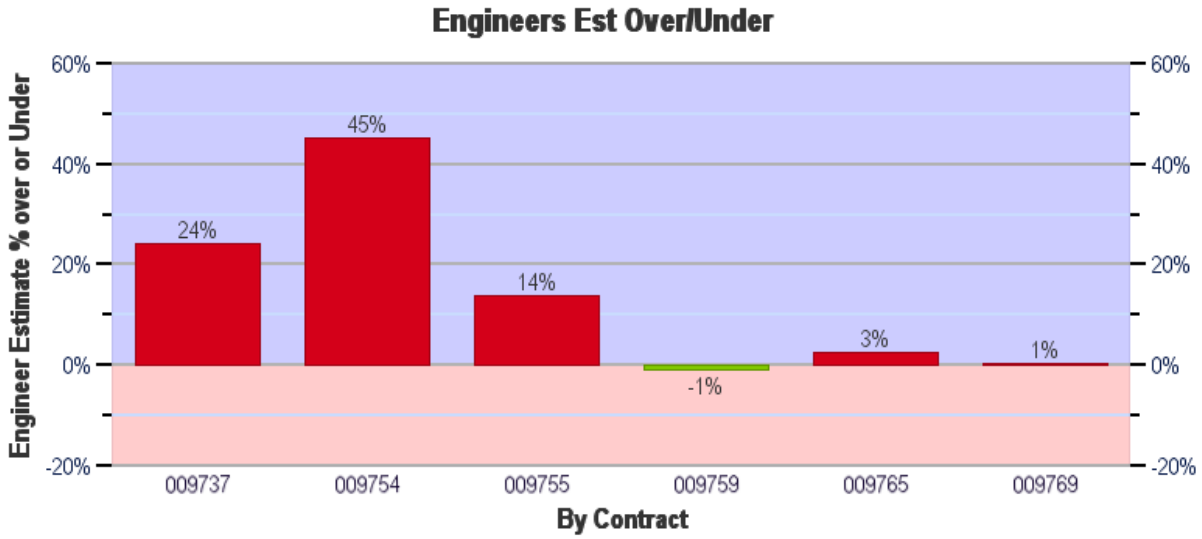

Data from January awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
April 2020 - March 2022

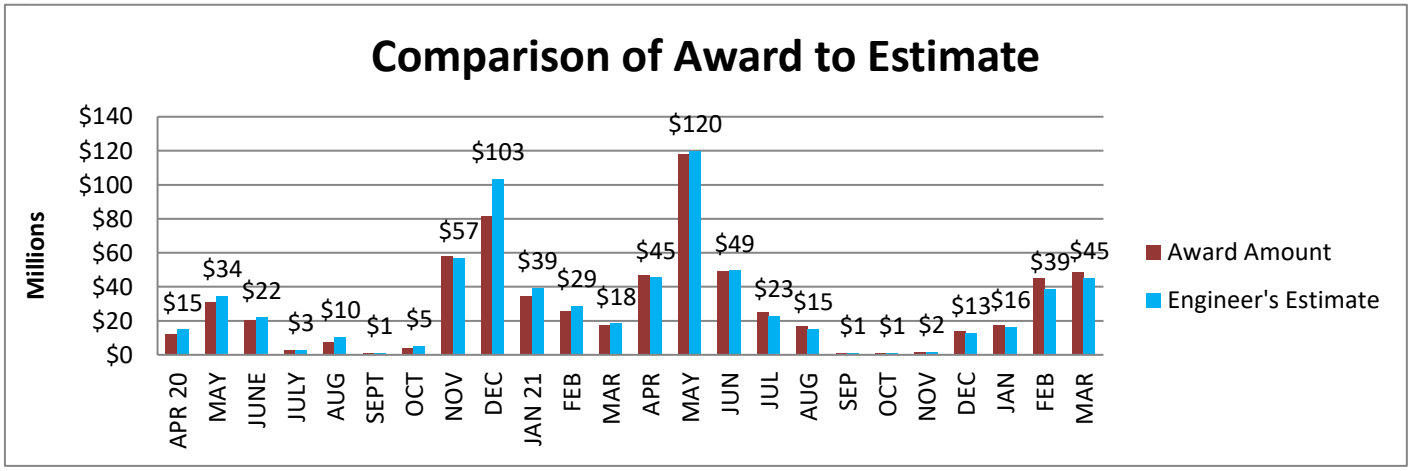

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
April-20	4	11	$14,815,642.00	$12,282,952.00	-17.1%
May	3	12	$34,337,191.00	$30,675,287.00	-10.7%
June	5	8	$21,904,179.00	$20,511,844.00	-6.4%
July	4	3	$2,502,440.00	$2,484,450.00	-0.7%
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
September	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
*January-22	4	4	$16,258,076.00	$17,566,886.00	8.1%
*February	4	6	$38,553,756.00	$45,096,911.00	17.0%
*March	3	12	$44,671,237.00	$48,547,539.00	8.0%

*Data not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison March 2022

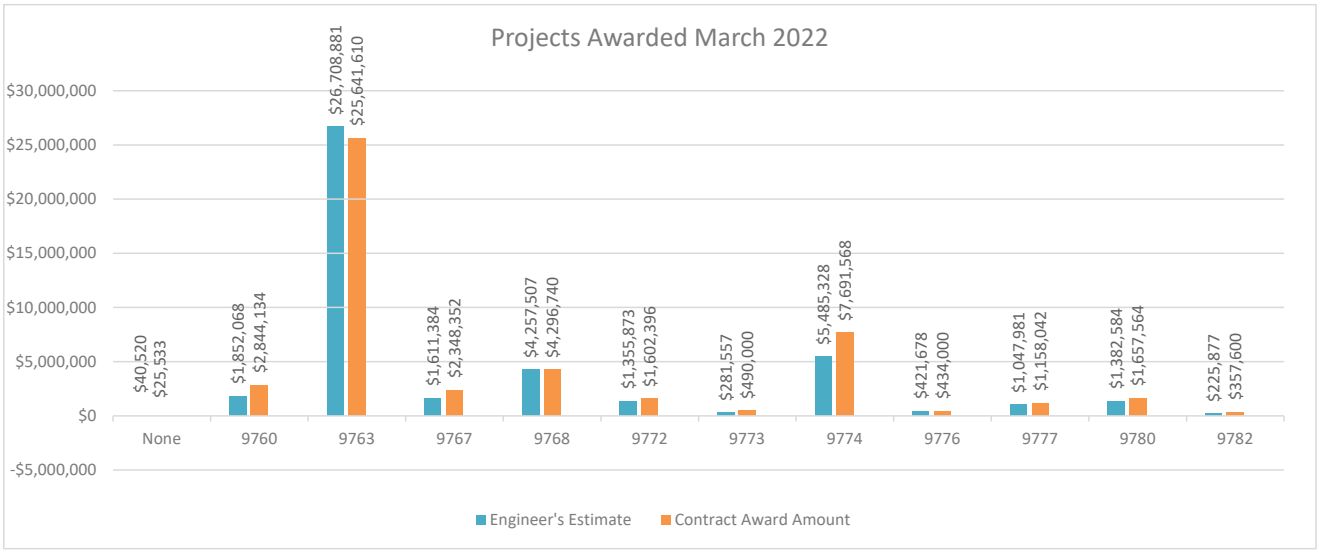

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
None	SR 204 Intersection Improv. Demo #	3/24/2022	2	$40,520	$25,533	-36.99%
9760	Us 395, Pasco -Flamingo Mobile Ho	3/3/2022	2	$1,852,068	$2,844,134	53.57%
9763	Sr 16 And Sr 302 (Spur), Purdy Cree	3/15/2022	11	$26,708,881	$25,641,610	-4.00%
9767	Sr 17, Grape Dr Intersection Safety	3/15/2022	2	$1,611,384	$2,348,352	45.74%
9768	Sr 410, 288th Ave Se Vic To Crystal	3/8/2022	4	$4,257,507	$4,296,740	0.92%
9772	Us 101, Delphi Rd To I-5 Paving And	3/11/2022	3	$1,355,873	$1,602,396	18.18%
9773	I-5, Jackson St & S Forest St Vic Fib	3/11/2022	2	$281,557	$490,000	74.03%
9774	Mudsen Creek -Remove Fish Barrie	3/18/2022	2	$5,485,328	$7,691,568	40.22%
9776	I-82, Coffin Rd Vicinity - Paving	3/22/2022	3	$421,678	$434,000	2.92%
9777	OR Strategic Bridge Preservation 21	3/23/2022	3	$1,047,981	$1,158,042	10.50%
9780	Us 101 / Hoquiam River, Riverside B	3/29/2022	2	$1,382,584	$1,657,564	19.89%
9782	Edmonds Ferry Terminal Paving Pre	3/22/2022	2	$225,877	$357,600	39.75%

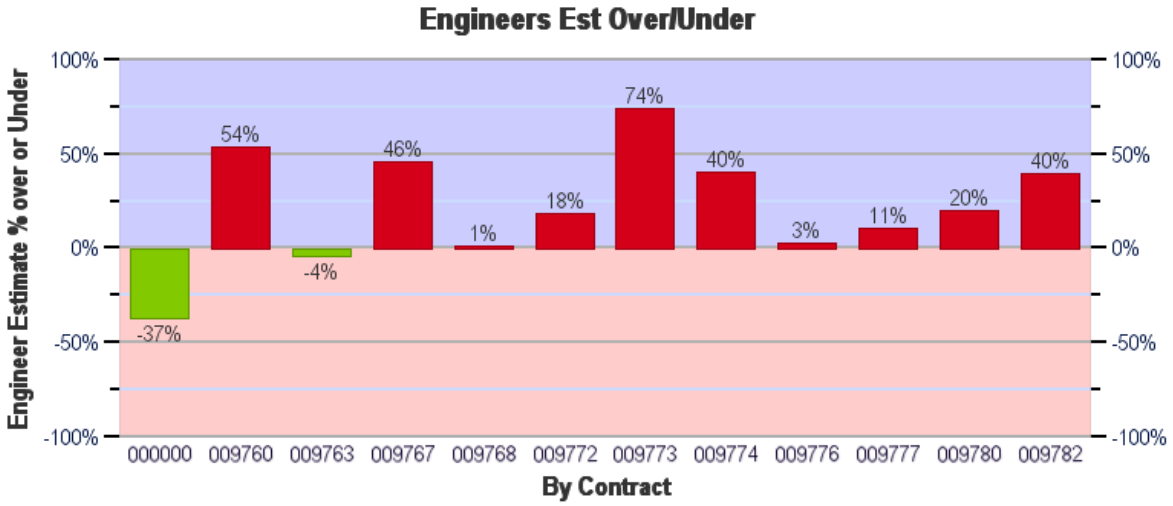

Data from March awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
May 2020 - April 2022

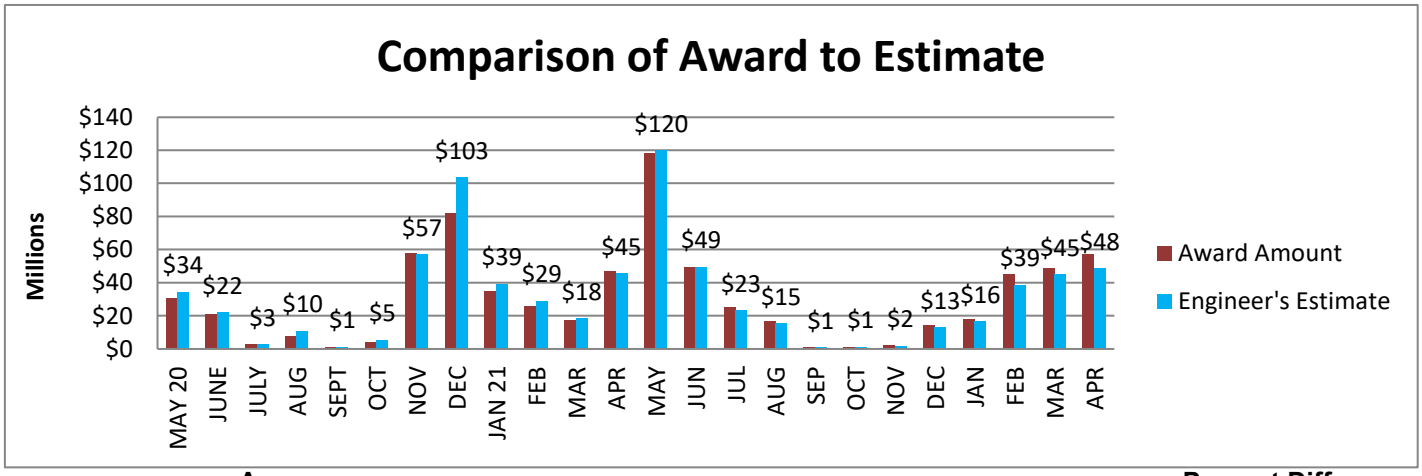

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
					-
June	5	8	$21,904,179.00	$20,511,844.00	-6.4%
					-
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
					-
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
-					-
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
					-
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
					-
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
					-
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
-					
*February	4	6	$38,553,756.00	$45,096,911.00	17.0%
*April	3	12	$48,412,332.00	$56,825,919.00	17.4%

*Data not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison April 2022

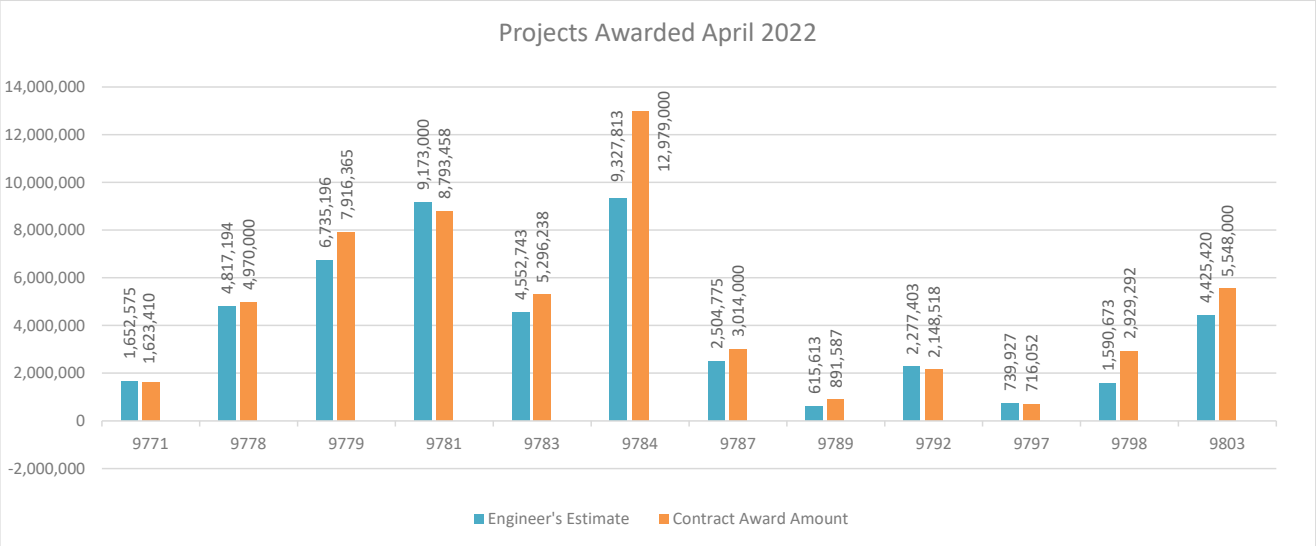

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9771	Sr 7, Sr 507 To S Of S 38th St Pavin	4/11/2022	3	$ 1,652,575	$ 1,623,410	-1.76%
9779	US 195 Old BNRR Bridge to Jct SR	4/6/2022	2	$ 6,735,196	$ 7,916,365	17.54%
9783	I-5, Northgate Way & Maple Rd Brid	4/8/2022	7	$ 4,552,743	$ 5,296,238	16.33%
9787	Sr 142, Lyle To Little Klickitat River B	4/20/2022	3	$ 2,504,775	$ 3,014,000	20.33%
9792	ER Bridge Deck Preventive Preserva	4/13/2022	1	$ 2,277,403	$ 2,148,518	-5.66%
9798	Bridge Deck Preventive Preservation	4/21/2022	1	$ 1,590,673	$ 2,929,292	84.15%

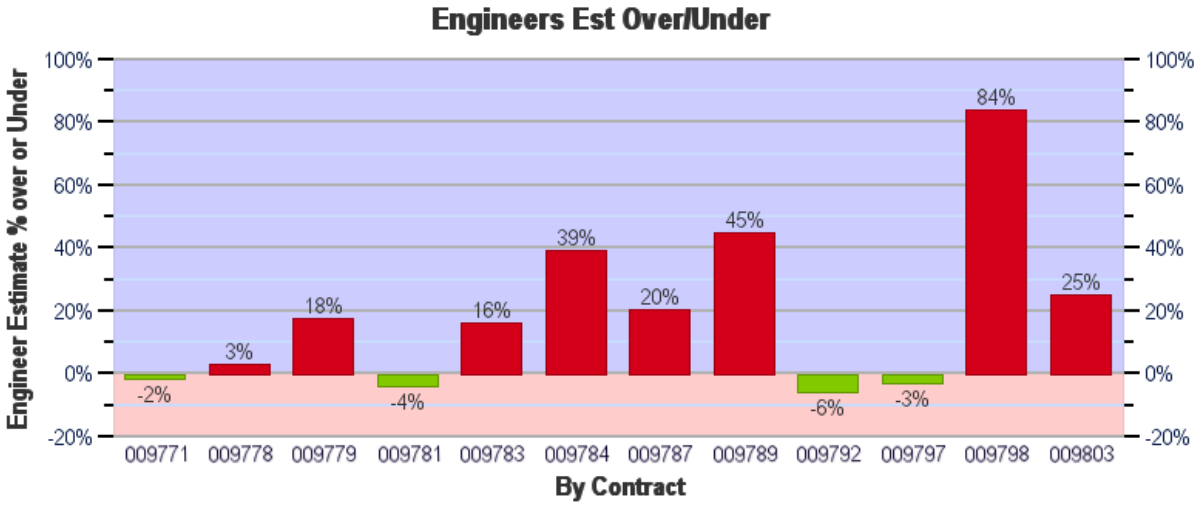

Data from April awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
June 2020 - May 2022

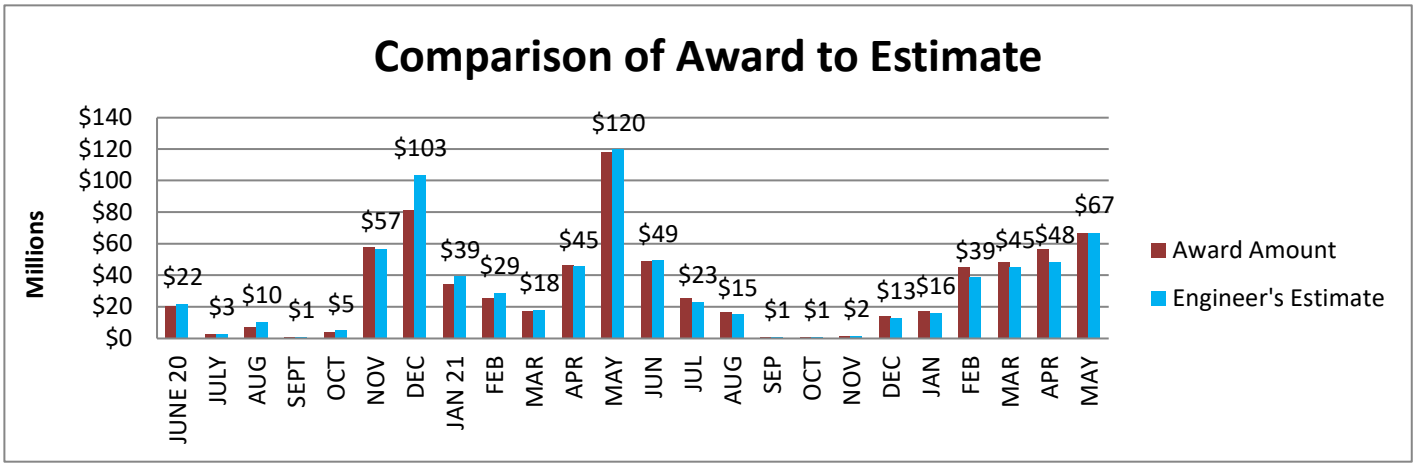

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
Jun-20	5	8	$21,904,179.00	$20,511,844.00	-6.4%
					-
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
					-
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
-					-
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
					-
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
					-
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
					-
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
-					
*February	4	6	$38,553,756.00	$45,096,911.00	17.0%
*April	3	12	$48,412,332.00	$56,825,919.00	17.4%
					-

*Data not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison May 2022

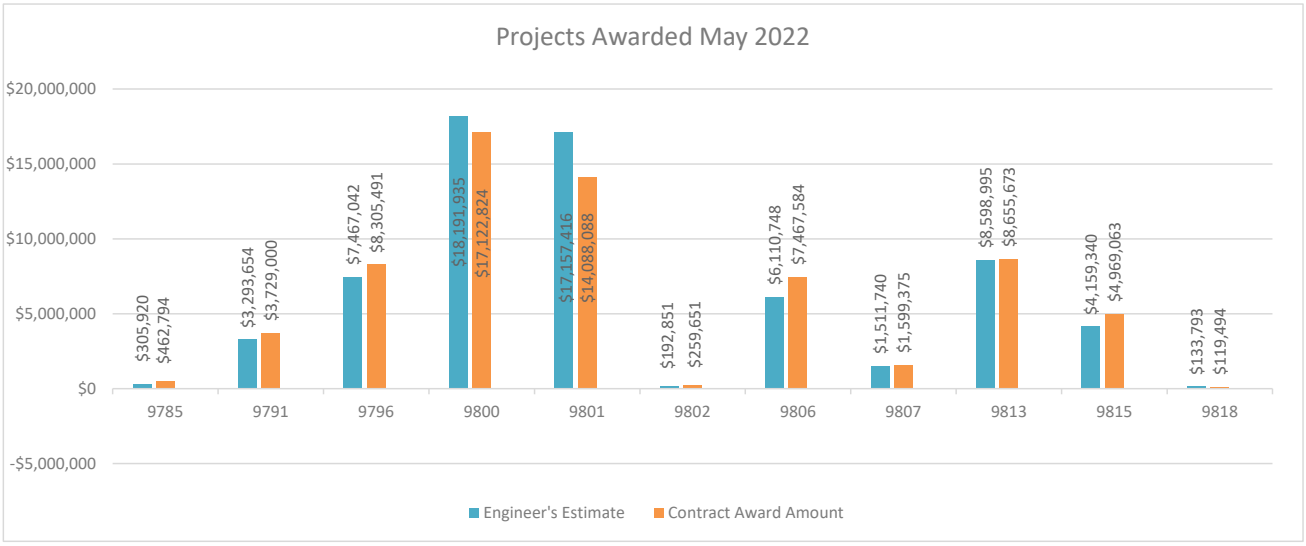

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9785	Tahlequah Ferry Terminal - Facility A	5/4/2022	2	$305,920	$462,794	51.28%
9791	Colville to Columbia River Paving	5/3/2022	2	$3,293,654	$3,729,000	13.22%
9796	Rocky Creek To Granite Creek BST	5/9/2022	2	$7,467,042	$8,305,491	11.23%
9800	I-205 To SE 164th Avenue Auxiliary	5/9/2022	3	$18,191,935	$17,122,824	-5.88%
9801	SR 204 Intersection Improvements S	5/26/2022	5	$17,157,416	$14,088,088	-17.89%
9802	East of Leavenwoth - Slope Stabiliza	5/9/2022	2	$192,851	$259,651	34.64%
9806	Stevens Pass East - Paving	5/26/2022	3	$6,110,748	$7,467,584	22.20%
9807	NE 182nd Ave Intersection Improvem	5/12/2022	3	$1,511,740	$1,599,375	5.80%
9813	Oaks Ave I/C to Yakima River Bridge	5/19/2022	2	$8,598,995	$8,655,673	0.66%
9815	2022 SCR Region Wide Chip Seal	5/19/2022	3	$4,159,340	$4,969,063	19.47%
9818	Belfair Area - Driveway Revision	5/19/2022	5	$133,793	$119,494	-10.69%

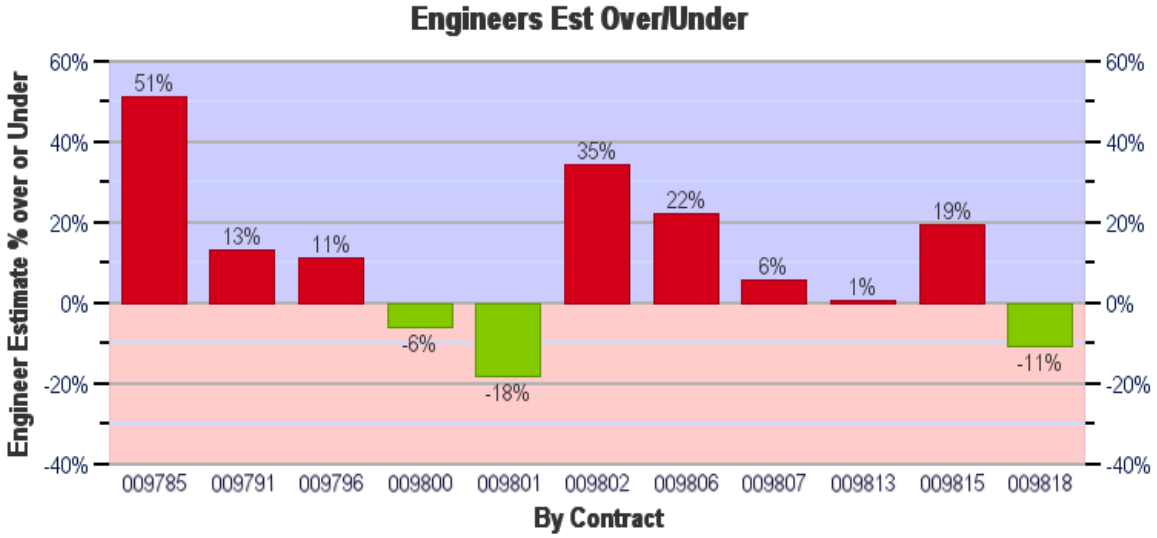

Data from May awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
July 2020 - June 2022

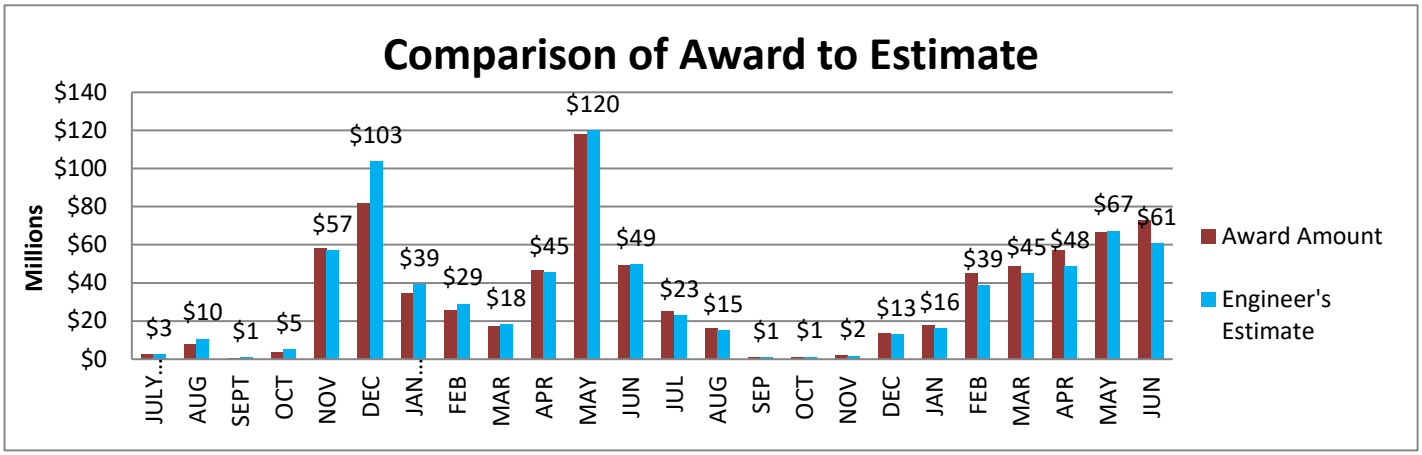

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
July	4	3	$2,502,440.00	$2,484,450.00	-0.7%
August	4	6	$10,409,043.00	$7,478,581.00	-28.2%
September	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
*January-22	4	4	$16,258,076.00	$17,566,886.00	8.1%
*February	4	6	$38,553,756.00	$45,096,911.00	17.0%
*March	3	12	$44,671,237.00	$48,547,539.00	8.0%
*April	3	12	$48,412,332.00	$56,825,919.00	17.4%
*May	3	11	$67,123,435.00	$66,779,036.00	-0.5%
*June	3	20	$60,590,380.00	$72,586,258.00	19.8%
**June	5	1	$249,464,179.00	$285,464,518.00	14.5%

*Data not available in CCIS

**Also opened in June: Contract 9786 Cabin Cr I/C to West Easton I/C Phase 3 Add Lanes and Wildlife Bridges.

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison June 2022

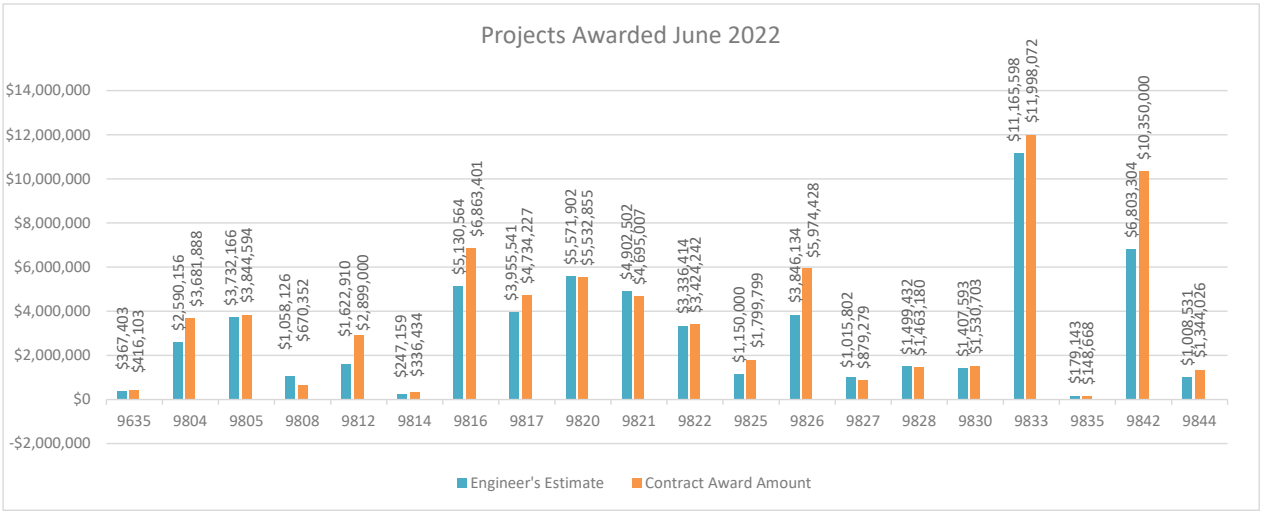

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9635	Mount Baker Tunnel Heat Detection System	6/27/2022	3	$367,403	$416,103	13.26%
9804	Duwamish River To S Spokane St Vic Pavin	6/7/2022	2	$2,590,156	$3,681,888	42.15%
9805	Dike Access W Br MP 22.7 & BNRR Br MP	6/3/2022	7	$3,732,166	$3,844,594	3.01%
9808	Mcallister Creek & Mud Bay Bridges Repair	6/9/2022	3	$1,058,126	$670,352	-36.65%
9812	21 - 23 SWR Regionwide Bridges Concrete	6/7/2022	2	$1,622,910	$2,899,000	78.63%
9814	Kincaid Sign Structure Replacement	6/14/2022	2	$247,159	$336,434	36.12%
9816	2022 OR Region Wide Chip Seal	6/13/2022	2	$5,130,564	$6,863,401	33.77%
9817	North of Sunnyside and I-82 I/C - Paving	6/7/2022	3	$3,955,541	$4,734,227	19.69%
9820	Selah Creek Bridge to Yakima Vicinity Pavin	6/15/2022	3	$5,571,902	$5,532,855	-0.70%
9821	Northwest Region HMA Crack Seal & Pavem	6/15/2022	3	$4,902,502	$4,695,007	-4.23%
9822	NE 162nd Ave to Leadbetter Rd Paving	6/10/2022	2	$3,336,414	$3,424,242	2.69%
9825	Northup Prewash Pad Retrofit NPDDES - N	6/27/2022	2	$1,150,000	$1,799,799	56.50%
9826	Olympic Peninsula Chip Seal	6/10/2022	2	$3,846,134	$5,974,428	55.34%
9827	Evans Creek Temp Bridge Removal	6/15/2022	3	$1,015,802	$879,279	-13.44%
9828	US 395 to RD 170 Paving	6/15/2022	3	$1,499,432	$1,463,180	-2.42%
9830	System Wide on-Call Off-Shore Maintenanc	6/27/2022	2	$1,407,593	$1,530,703	8.75%
9833	E Sunset Way Vic & NB Lowell Rd Vic PCC	6/21/2022	3	$11,165,598	$11,998,072	7.46%
9835	Kingston Ferry Terminal Transfer Span Ove	6/2/2022	2	$179,143	$148,668	-17.01%
9842	Loon Lake to Hafer Rd Paving	6/29.2022	2	$6,803,304	$10,350,000	52.13%
9844	West Easton to Renslow Vicinity Bridge Dec	6/29/2022	3	$1,008,531	$1,344,026	33.27%
*9786	Cabin Cr I/C to W Easton I/C Phase 3 Add L	6/22/2022	5	$249,346,179	$285,464,518	14.49%

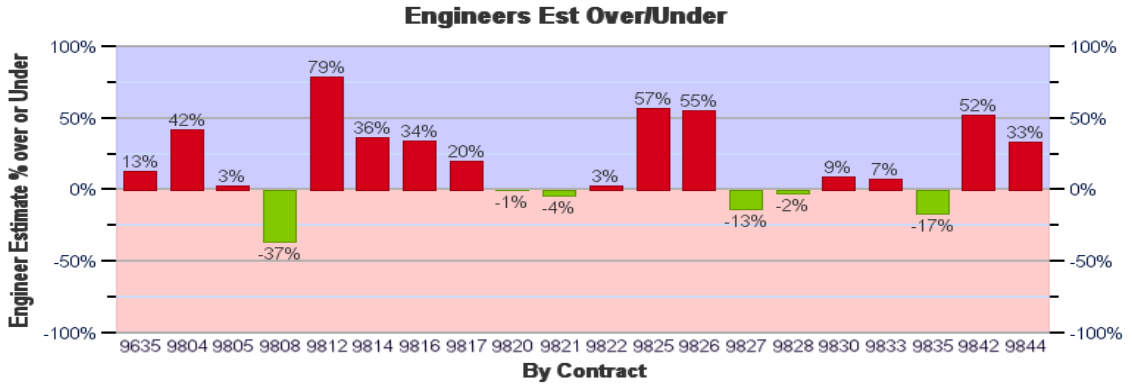

*Contract 9786 is not included in graphs

Data from June awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
August 2020 - July 2022

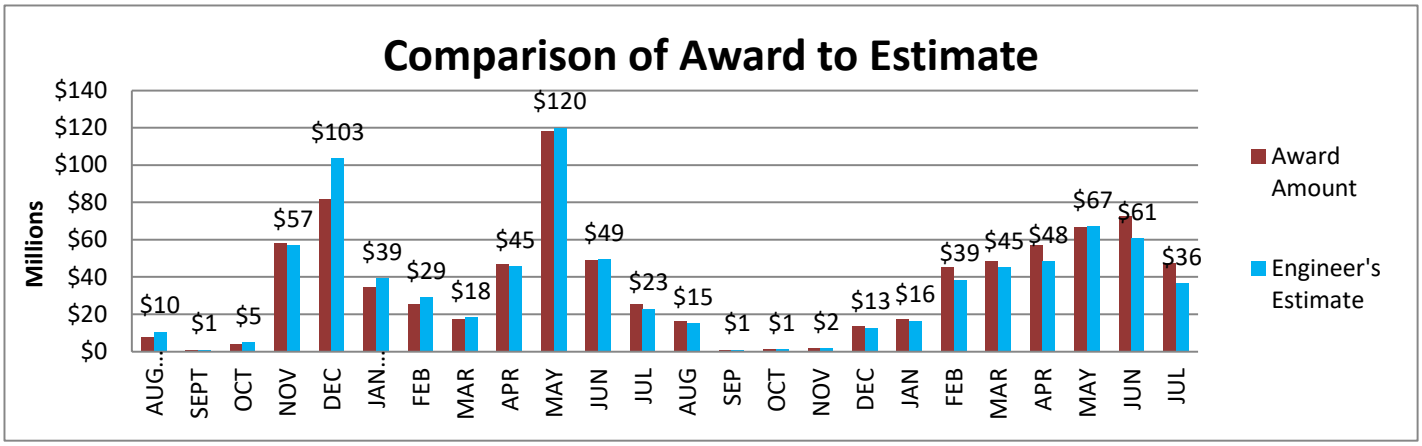

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
August-20	4	6	$10,409,043.00	$7,478,581.00	-28.2%
September	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
*October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
*November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
*January-22	4	4	$16,258,076.00	$17,566,886.00	8.1%
*February	4	6	$38,553,756.00	$45,096,911.00	17.0%
*March	3	12	$44,671,237.00	$48,547,539.00	8.0%
*April	3	12	$48,412,332.00	$56,825,919.00	17.4%
*May	3	11	$67,123,435.00	$66,779,036.00	-0.5%
*June	3	20	$60,590,380.00	$72,586,258.00	19.8%
**June	5	1	$249,464,179.00	$285,464,518.00	14.5%
*July	3	10	$36,494,971.00	$47,385,519.00	29.8%

*Data not available in CCIS

**Also opened in June: Contract 9786 Cabin Cr I/C to West Easton I/C Phase 3 Add Lanes and Wildlife Bridges.

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison July 2022

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9829	Oregon State Line to Military Rd Vic Paving,	7/20/2022	3	$4,659,401	$5,945,000	27.53%
9832	I-90, Homestead Valley Rd To Hyak Bridge	7/7/2022	3	$1,544,600	$2,563,247	65.95%
9839	Eagle Harbor Maintenance Facility Slip F Dr	7/6/2022	5	$5,231,367	$5,116,468	-2.20%
9840	I-90, S Cle Elum Rd Bridges - Deck Rehabil	7/18/2022	3	$13,450,838	$14,589,091	8.46%
9841	I-5 And I-205, Concrete Panel Replacemen	7/5/2022	1	$2,778,165	$6,376,376	129.52%
9843	Us 2, Cashmere East Paving	7/7/2022	2	$5,043,602	$6,956,734	37.93%
9845	Kittitas & Yakima Co SE WA Centerline Rum	7/6/2022	2	$1,264,890	$2,530,479	100.06%
9846	NB 12th Street NE Girder Replacement	7/15/2022	2	$950,755	$1,472,060	54.83%
9849	Us 12, West Of White Pass- Repair Cable N	7/8/2022	2	$552,952	$596,064	7.80%
9854	Emergency Pavement Repair	7/14/2022	2	$1,018,402	$1,240,000	21.76%

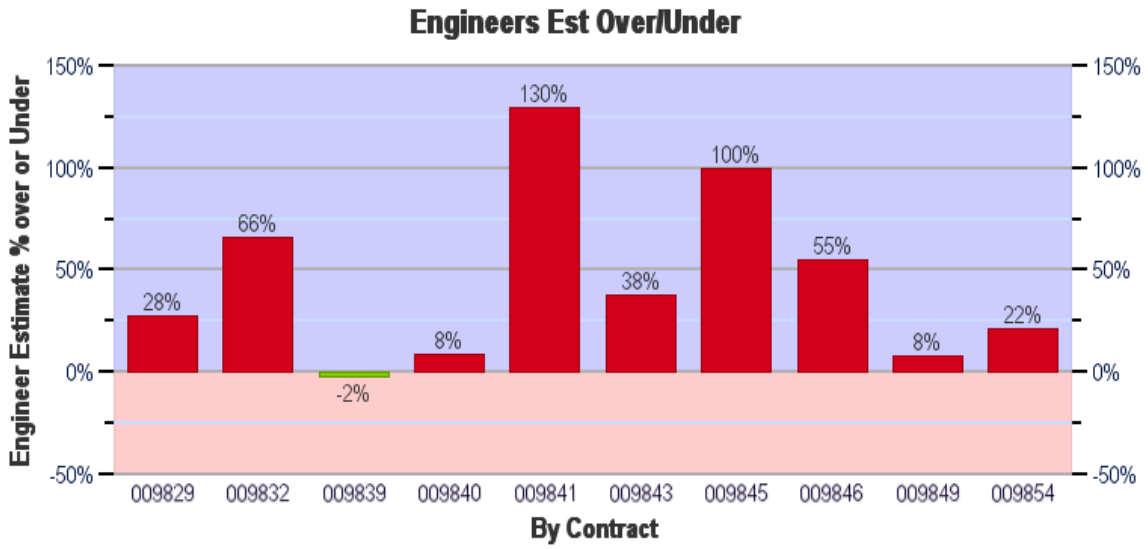

Data from July awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
September 2020 - August 2022

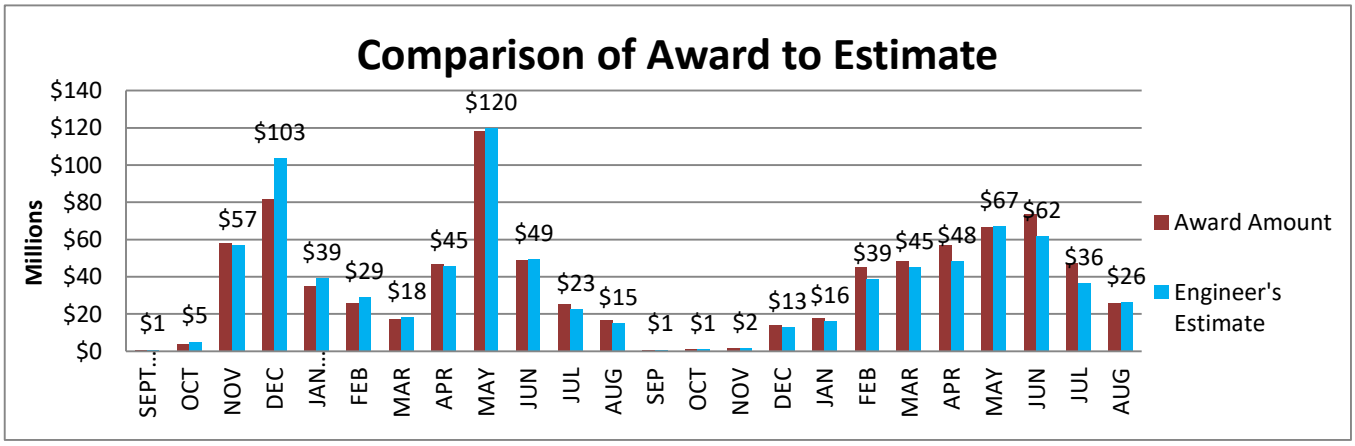

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
September-20	4	2	$815,020.00	$728,554.00	-10.6%
October	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
January	4	4	$16,258,076.00	$17,566,886.00	8.1%
February	4	6	$38,553,756.00	$45,096,911.00	17.0%
March	3	12	$44,671,237.00	$48,547,539.00	8.0%
April	3	12	$48,412,332.00	$56,825,919.00	17.4%
May	3	11	$67,123,435.00	$66,779,036.00	-0.5%
*# June	3	20	$60,590,380.00	$72,586,258.00	19.8%
**June	5	1	$249,464,179.00	$285,464,518.00	14.5%
*July	3	10	$36,494,971.00	$47,385,519.00	29.8%
*August	4	5	$26,207,213.00	$25,859,593.00	-1.3%

*Some data not available in CCIS

*# Data updated after CCIS updated

**Also opened in June 2022: Contract 9786 Cabin Cr I/C to West Easton I/C Phase 3 Add Lanes and Wildlife Bridges.

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate ComparisonAugust 2022

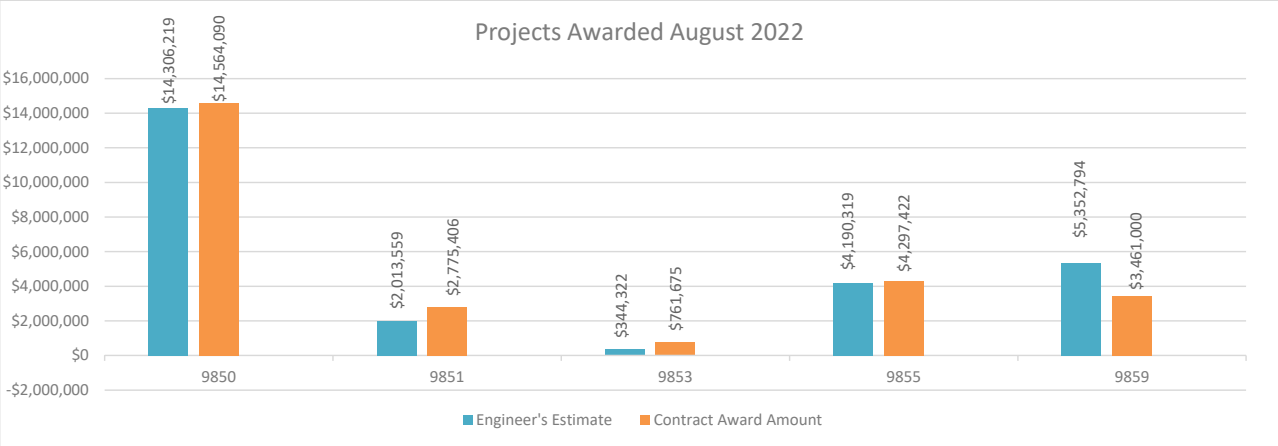

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9850	I-405, Bn Rr Bridge To Ped Trail Bridge Seis	8/15/2022	5	$14,306,219	$14,564,090	1.80%
9851	Sr 18 Et Al, Northwest Region Hma Crack S	8/8/2022	3	$2,013,559	$2,775,406	37.84%
9853	Sr 524, Locust Way Vic To Larch Way Vic D	8/5/2022	1	$344,322	$761,675	121.21%
9855	I-90 Et Al, Scr Region Wide - Roadside Hard	8/8/2022	4	$4,190,319	$4,297,422	2.56%
9859	Sr 526, Airport Rd To E Casino Rd Seismic	8/16/2022	5	$5,352,794	$3,461,000	-35.34%

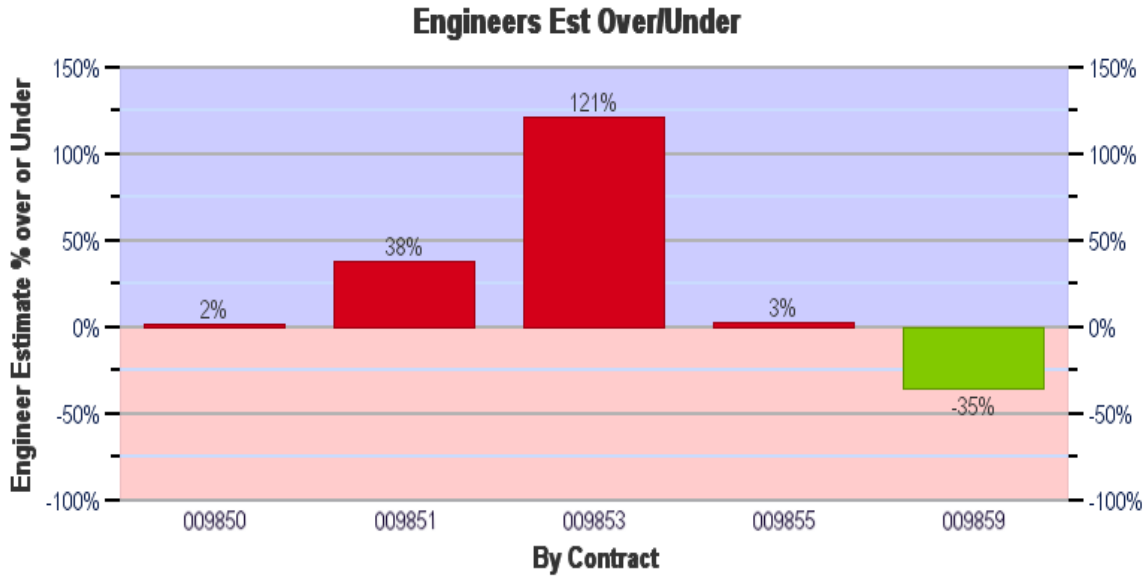

Data from July awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Awarded Design Bid-Build Contracts: Award to Estimate with Average Number of Bidders by Month
October 2020 - September 2022

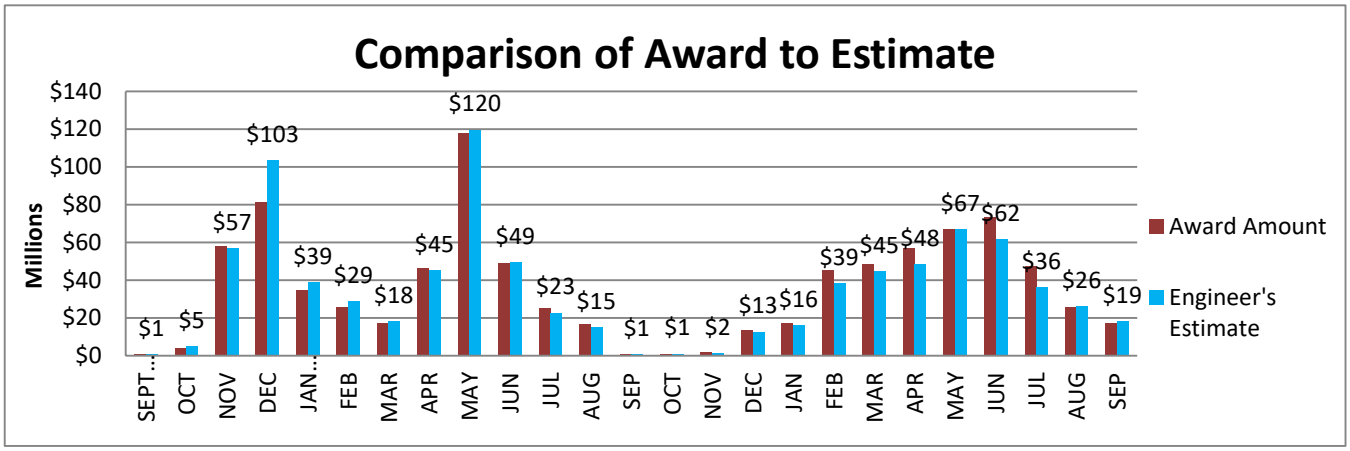

Month	Average Number of Bidders	Number of Projects	Engineer's Estimate	Contract Award Amount	Percent Difference Between Estimate and Award
October-20	5	4	$4,999,176.00	$3,910,663.00	-21.8%
November	4	6	$56,977,221.00	$57,966,138.00	1.7%
December	5	12	$103,483,514.00	$81,525,699.00	-21.2%
January-21	4	12	$39,172,832.00	$34,613,080.00	-11.6%
February	4	8	$28,861,805.00	$25,599,455.00	-11.3%
March	4	11	$18,183,611.00	$17,200,183.00	-5.4%
April	4	15	$45,490,765.00	$46,553,976.00	2.3%
May	3	13	$119,798,071.00	$118,011,329.00	-1.5%
June	4	12	$49,420,914.00	$49,078,954.00	-0.7%
July	3	7	$22,843,885.00	$25,181,875.00	10.2%
August	4	3	$15,135,192.00	$1,646,492.00	8.8%
September	2	4	$896,752.00	$831,912.00	-7.2%
October	2	3	$1,066,373.00	$1,046,953.00	-1.8%
November	5	2	$1,610,870.00	$1,773,107.00	10.1%
*December	3	6	$12,860,167.00	$13,833,317.00	7.6%
January	4	4	$16,258,076.00	$17,566,886.00	8.1%
February	4	6	$38,553,756.00	$45,096,911.00	17.0%
March	3	12	$44,671,237.00	$48,547,539.00	8.0%
April	3	12	$48,412,332.00	$56,825,919.00	17.4%
May	3	11	$67,123,435.00	$66,779,036.00	-0.5%
*# June	3	20	$60,590,380.00	$72,586,258.00	19.8%
**June	5	1	$249,464,179.00	$285,464,518.00	14.5%
*July	3	10	$36,494,971.00	$47,385,519.00	29.8%
*August	4	5	$26,207,213.00	$25,859,593.00	-1.3%
*September	4	6	$17,153,854.00	$18,556,759.00	-7.6%

*Some data not available in CCIS

*# Data updated after CCIS updated

**Also opened in June 2022: Contract 9786 Cabin Cr I/C to West Easton I/C Phase 3 Add Lanes and Wildlife Bridges.

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov

Monthly Award to Estimate Comparison September 2022

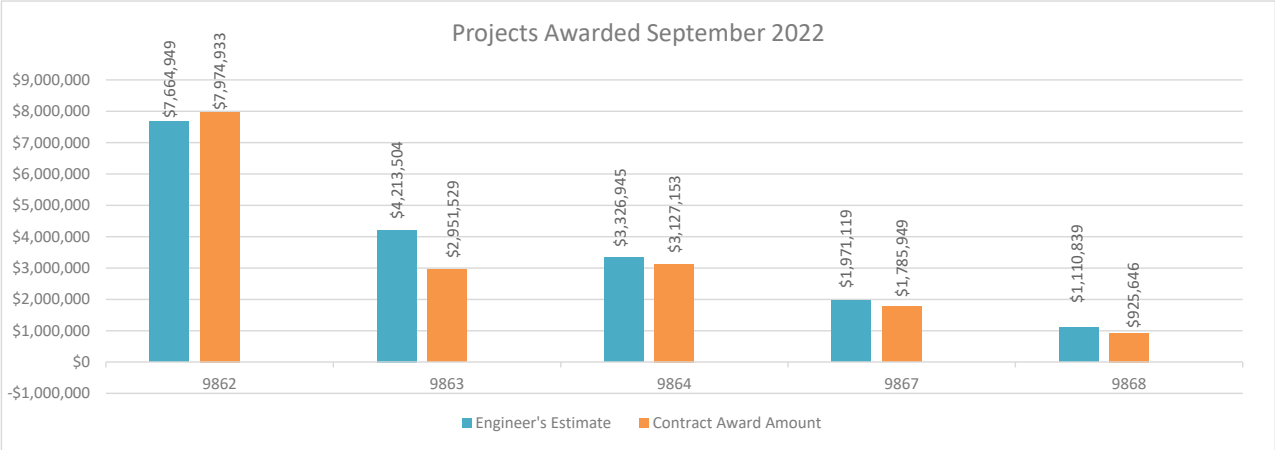

Contract Number	Title	Award Date	Number of Bidders	Engineer's Estimate	Contract Award Amount	Over / Under Percent
9862	East Jefferson County Remove Fish Barriers	9/30/2022	7	$7,664,949	$7,974,933	4.04%
9863	Hood Canal Bridge Replace Pontoon Hatche	9/20/2022	7	$4,213,504	$2,951,529	-29.95%
9864	Strategic Concrete Bridge Deck Preservatio	9/19/2022	4	$3,326,945	$3,127,153	-6.01%
9867	Twanoh Creek - Remove Fish Barrier	9/22/2022	4	$1,971,119	$1,785,949	-9.39%
9868	Vantage - Upgrade ITS Components	9/29/2022	3	$1,110,839	$925,646	-16.67%
9877	Cle Elum River Bridges Phs. 2 Roadside Re	9/28/2022	1	$278,404	$388,644	39.60%

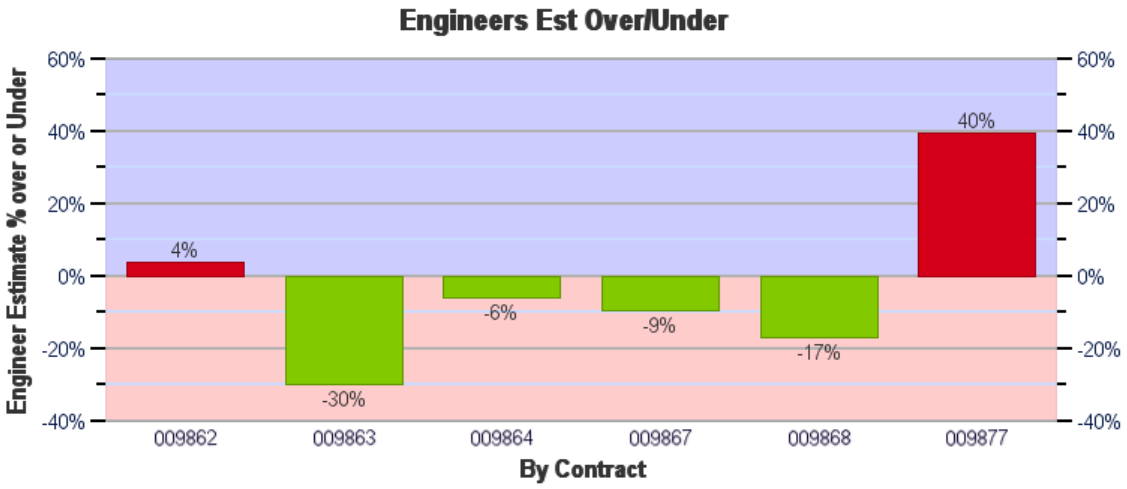

Data from September awards currently not available in CCIS

Note: Does not include Design Build, Emergency Contracts, On-Call, Single Source or Region Level Small Works Projects

Washington State Department of Transportation

For more information, please contact Kari Beardslee from the WSDOT Design Office at beardsk@wsdot.wa.gov
